

## Weekly Report No. 71 July 19<sup>th</sup>, 2021 through July 24<sup>th</sup>, 2021

Wahconah Regional High School  
150 Old Windsor Road, Dalton, MA 01226

### **Safety:**

As of July 24<sup>th</sup>, 2021, the project has 11 consecutive safe working days. A painter had fallen and hurt his leg last week and has not returned to work, ergo a lost time accident. Barr & Barr is checking his status and will report additional information as it becomes available.

### **Covid-19 Protocols**

COVID-19 Protocols have been modified to comply with the most up to date mandates required by the state of Massachusetts. There were no COVID-19 related incidents to report this week.

### **Manpower**

Manpower was strong with . The average Daily man count was 116 with 51 working on Saturday.

### **Barr & Barr:**

Continues to have a fulltime PM and Superintendent and several assistant superintendents along with 3 laborers and a carpenter.

### **Allied Testing**

Was not on site this week, Sidewalks and completion of the Entrance SOG should be ready this week baring another week of Monsoon like rainfall.

### **Adams Plumbing**

Is finishing the kitchen equipment connections and fixture installation throughout the school.

### **Ayotte & King**

Two men Wednesday, Thursday and Friday installing Epoxy Flooring in the Janitorial Utility Rm.

### **Champlain Masonry**

Was not on site this week

### **Chandler Architectural**

Chandler worked with an average crew size of 8 Installing the School-guard glass in the Main Entry, the Learning Commons and the Window Shades. Chandler also worked 10 men on Saturday.

### **CJM**

CJM had a crew of 2 workers during the week they were working on the installation of flooring in C1 and D1. 7/19/21. Ongoing

### **Dobbert Fire Protection**

Dobbert is down to just their foreman working on installation of sprinkler heads in the ceilings as the grid is installed.

### **General Mechanical Contractors**

Is working on RGD'S, Refrigeration Piping, Chiller start up Controls and Insulation.

## **Greenfield Glass**

Was not on site this week

## **H. Carr.**

H Carr was focused on the Auditorium Ceiling Framing and layout all week with a 7 person crew.

## **Higgins**

Had a crew of 6 workers Installing Tile in C1 and D1 Bathrooms, Accent Tile in C2 and D2 and Locker Room Tile.

## **Island International.**

Was not on site this week.

## **JD Rivet Roofing**

Worked on metal roof edge and other details with a crew of 4 on Wednesday and 2 on Thursday and Friday.

## **J.H. Maxymillian:**

Worked a crew of 4 all week raising the grades at the East and West elevations and prepping for bituminous access road base this week.

## **Marguerite Concrete:**

Crew of 4 worked all week on layout and forms for the Main Entrance Exposed Aggregate sidewalk. No concrete was poured this week.

## **Northeast Painting**

Had as many as 7 painters working all over the building, including door frames, 2<sup>nd</sup> coat in classrooms and Custodians office space.

## **Nor'easter Installations**

Four men on site installing casework in the classrooms in Area D2 and D1. Ongoing

## **Professional Drywall Corp**

PDC'S crew is down to 5 working on odds and ends, Entrance Vestibule, Admin ceilings, Soffits in the East and West Entranceways.

## **Universal Electric**

Universal had an average crew of 23 this week working in almost every area of the project notably the Classroom Lights in C1, D1, Auditorium Lighting, Energize Panels, Lighting on Main Street and PV Array on the gym. The count also includes their Sub Subs Wel-Design (AV Systems), RGS (Low Voltage Wiring) and Johnson Controls (BMS Installations) Universal also had 12 Electricians on site Saturday. Ongoing.

## **Ralph's Blacksmith**

Came back to the site with a 3 man crew installing metal railings on the stairways. See pictures above.

## **Westek**


Had a crew doing installation of the Sound Baffles in the Auditorium and Installing Display Cases on Main Street.

## **Meetings**

The next weekly construction meeting scheduled for Wednesday 7/28/21. Via Web Ex.



7/19 Overcast, Wet, Soggy

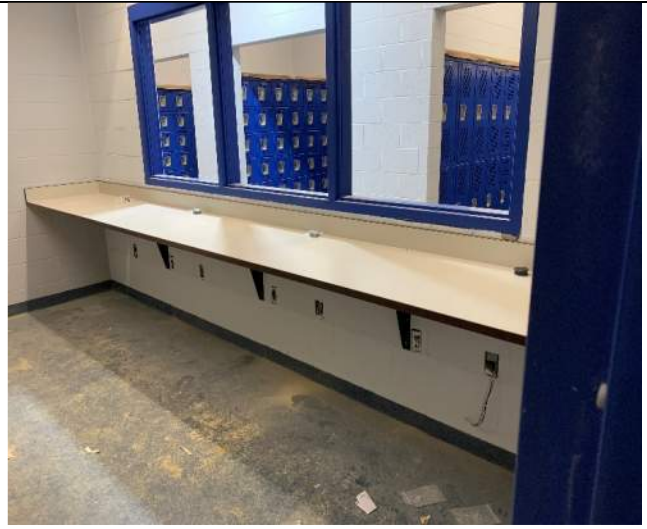

7/19 Coaches Office, Girls Locker Room



7/20 Plantings at Student Parking Lot



7/20 Grade Raising West Elevation



7/21 West Side Compacted for Bituminous Base



7/21 Framing for Exposed Aggregate Concrete at the Main Entrance





7/22 Exposed Aggregate Concrete Outdoor Seating Area. Beautiful!



7/22 Looking out from Student Commons



7/22 Greenhouse Nearing Completion



7/22 Stair 2 Railing System Installation




7/23 Rail System Installed



7/23 Entrance Formed and Ready for Concrete



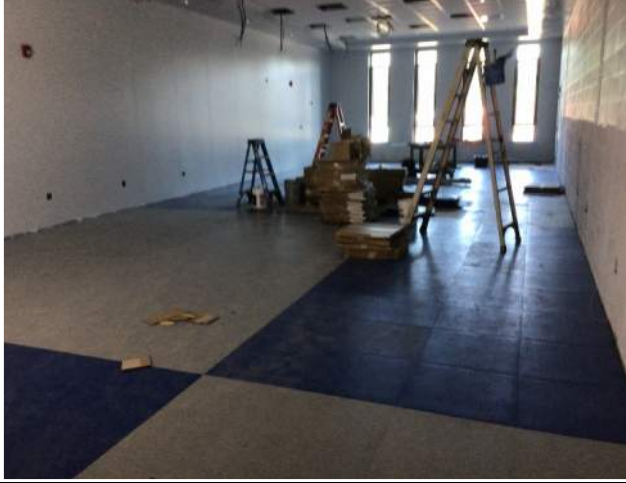

7/23 Fitness Room Floor Installation



7/23 Main Street Floor Tile Installation Begins



7/23 Landscape Trees Delivered



7/22 Band Room Lighting Installed



7/24 South Entrance Looking Down from C2



7/24 Main Street Clean Up
